


Foundation		Framing & Exterior		Interior		Foundation		Framing & Exterior	
1 week	2 weeks	3 weeks		1 week	2 weeks				
30000		70000		100000		30000		70000	
6 weeks						6 weeks			

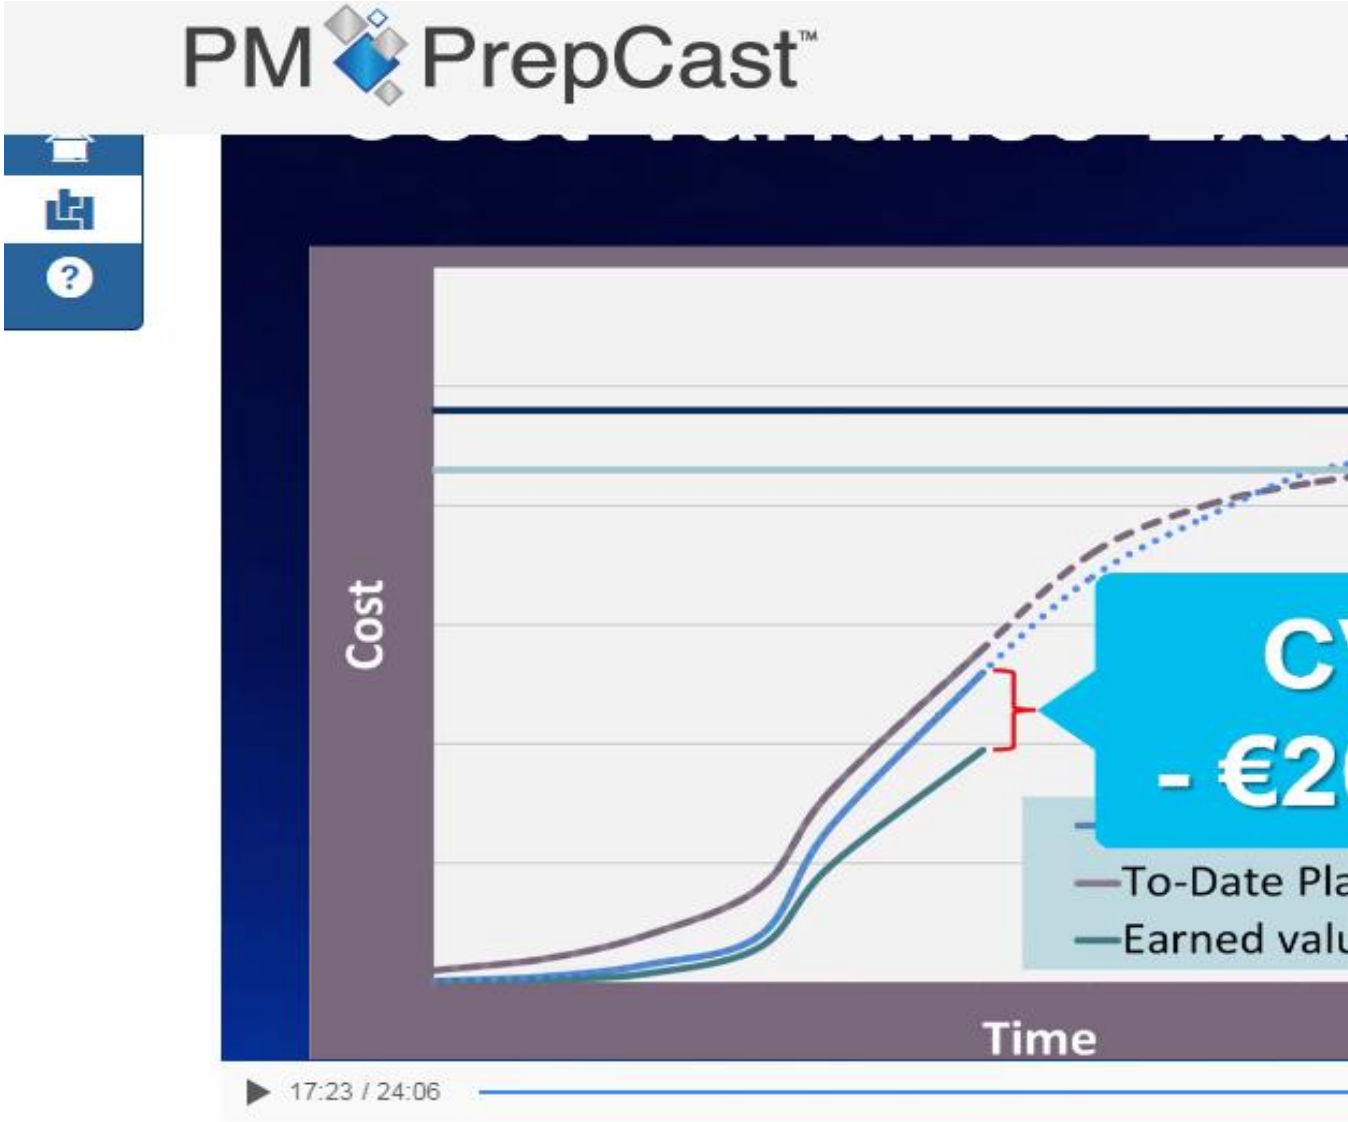

After 14 weeks

PV = 46500((200000+200000+30000+35000(half


EV = 43000((200000+200000+30000)



Interior	Foundation	Framing & Exterior		Interior		
3 weeks	1 week	2 weeks		3 weeks		
100000	30000	70000		100000		
Weeks	week 13	week14	week15	week 16	week 17	week 18
	foundation complete					
from 2 weeks of 70000))						


Hello, Narcis Turculet!


◀ Prev
Next ▶
Contents



- After 14 weeks
 - PV = €430,000
 - EV = €400,000
 - AC = €420,000
- $CV = EV - AC$
- CV is not budget variance

V =
0,000

anned Value
ue

